


OVERALL PLAN JAN-DEC  
2024

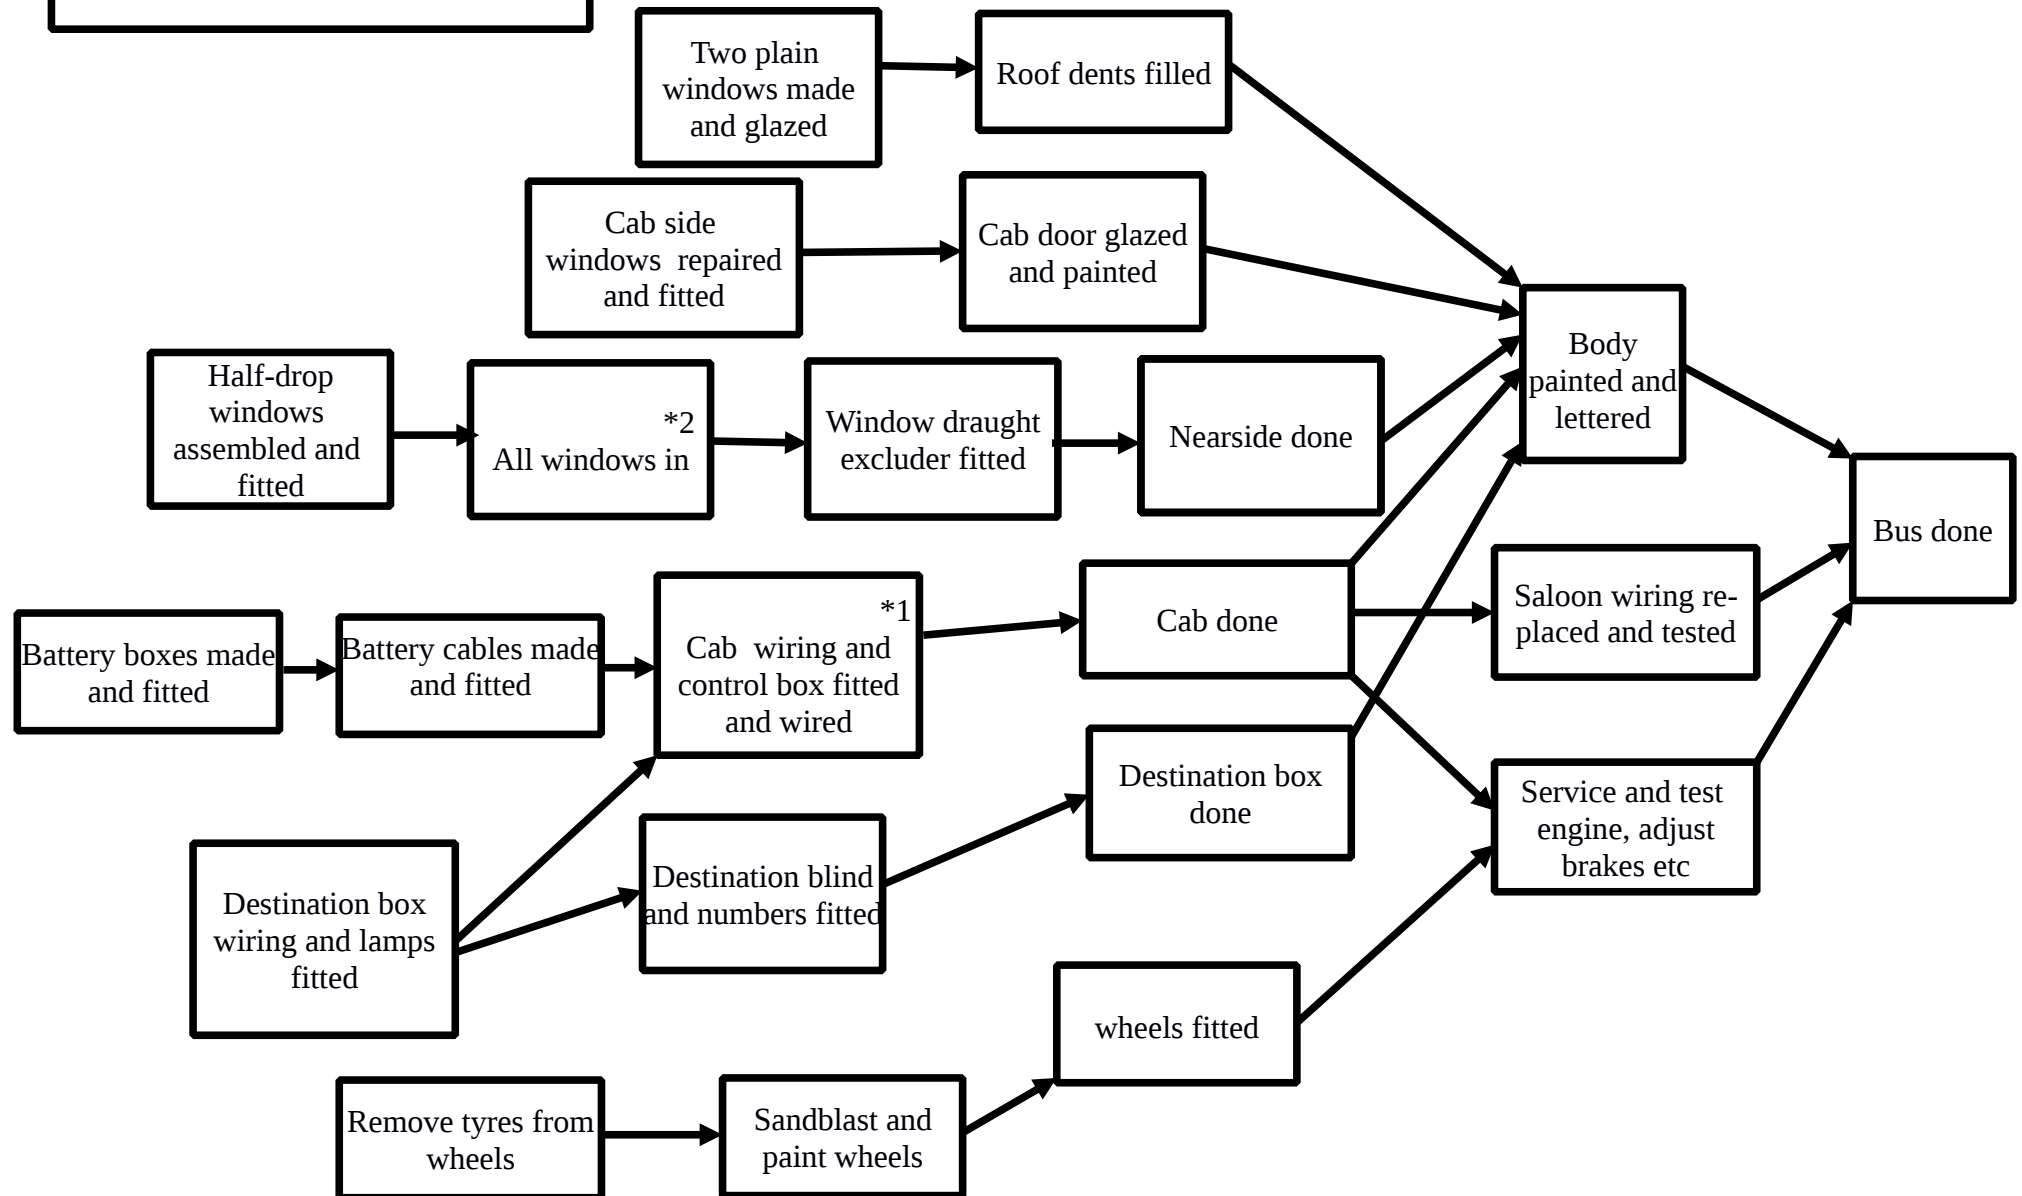

\*1 Refer to cab point-to-point wiring schedule

\*2 Windows:

1. Frames to be tried in openings to determine any trimming required.
2. Windows need to be “chromed” then assembled.
3. Fixed window aft of cab needs a new frame manufacturing.
4. Rearmost fixed window needs glass to be sourced and fitted in frame
5. Emergency door window frame needs to be repaired or remade
6. 1x lower edge channel needs making

Order of priority

Chrome window uprights and fit felt

Manufacture new frame for first window.

Assemble and fit windows
